

Builders for Christ

Weekly Update from
Immanuel Lutheran School, Hutchinson, MN

October 24, 2023

Hi all,


I went to Hutchinson today to visit “our baby”. She’s looking good! All of the exterior “storefront” doors have been installed. If you see on the pictures that there’s some glass missing it is because the electrician needs to wire the door releases before the glass can be installed. That way the doors can be locked and the receptionist can release the lock remotely allowing people to enter. The glass is missing on the back door because the temporary power is still routed through there. That will be taken care of next week.



Stone sills still haven’t been installed between the stone and siding or windows. The first layer of pavement has been applied to the parking lot. No definite word yet on exact dates for bathroom partitions and grab bars. It will be after the ceramic tile is on the walls and that’s not on the schedule yet either.

Peridot signup is now available on the KW website. Please consider coming in March and/or April. January and February filled up fast but we’re way short of help yet in March and April. God Bless!

In His service,
Elwood Heldt
507-327-331

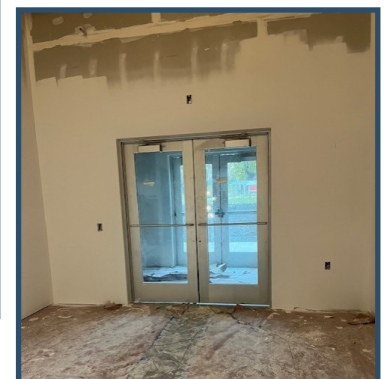

I went there today to help the new superintendent tear out the metal lath and tar paper



above the back storefront door. It was originally designed to have the stone sill cap above there, but they decided they didn’t like that there so we put a frieze board there instead. You can see it on the picture.

Inside painting is ongoing and there is taping and mudding going on also. Floors are scheduled to be stained Thursday and Friday of this week and all the Interior doors are to arrive on Monday the 30th. Some of us will be returning on the 6th of November to begin installing the doors. Ceiling grid and cabinet installation are all set to begin on that same day. It’s a big building, I don’t think we’ll get in each other’s way.
