

# Builders for Christ

Update from  
Immanuel Lutheran School, Hutchinson, MN

**November 10, 2023**


Hi Volunteers and other interested parties,

A crew of 4 finished hanging and accessorizing all but one door by Wednesday afternoon. I think we all learned new things about panic bars, overhead stops, closers and dutch doors. Unfortunately, I probably won't remember those things when I need to do it next time. I thank God for the talents and patience of those that were there this week! I'm a framer, not a finish carpenter. The one door we couldn't do is the one to the storm shelter/conference room because it is a special order and still on it's way.

Permanent power was delivered to the building on Wednesday, so now the gas line can be hooked to the roof top heaters and heat is expected early next week. The big pile of clay that was removed for the soil correction is being hauled away.



Look below and see that I have included some pictures of the cabinets installed in the classrooms. They are looking good! On Thursday the lockers were delivered and installation of those began. The super sent me a picture of that so I could include it in the newsletter.

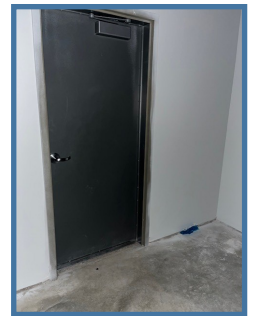

Painters will return once the heat is on and I think they will be upset that we have the doors on already but the super wanted it done and we had the crew to do it.



Ceramic tile installation should begin Monday the 13<sup>th</sup>. The super wants to give them plenty of time to get that done before we arrive to install bathroom partitions, handicap bars, tp dispensers, towel dispensers etc. He has asked that we plan on doing that starting December 4<sup>th</sup>.

That should catch you up on what is going on at Immanuel, Hutchinson. I don't know if there will be any more updates before we return in December. Thanks for your interest. God Bless!

In His service,  
Elwood Heldt

